


EC Module Prod. Schedule

- Restart the exercise in order to
 - ✓ Find possible problems
 - ✓ Determine the right component delivery and distribution
 - ✓ Optimize the flavour swapping in sites producing different type


Current status and estimate

- One month delay w.r.t last SCT estimates
- All sites finishing by April 2005


Old

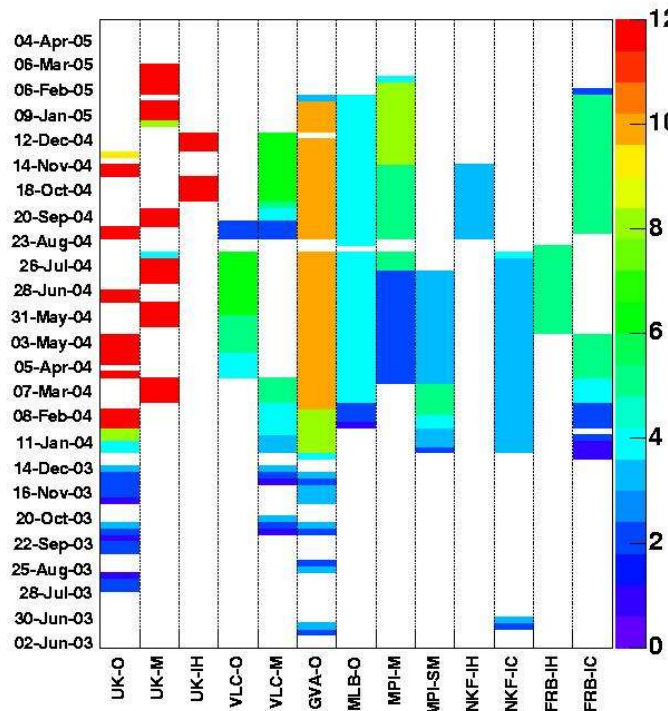

Current

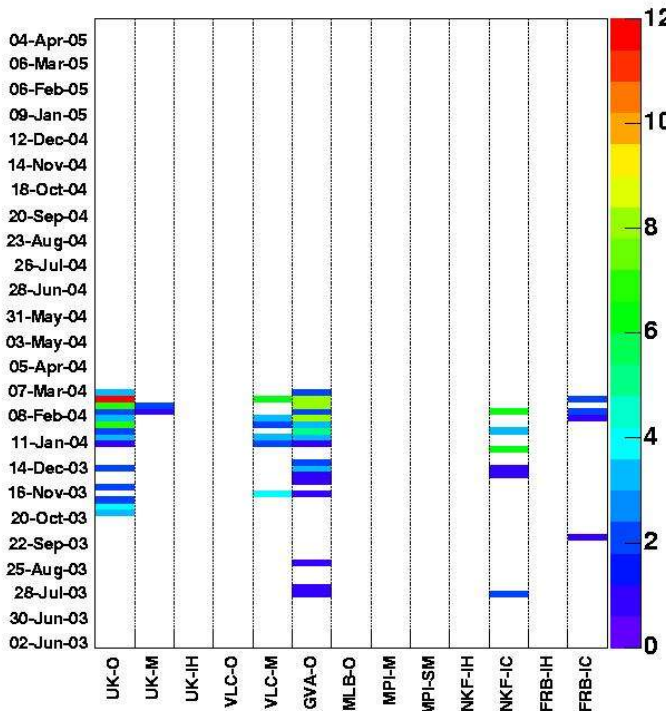


New

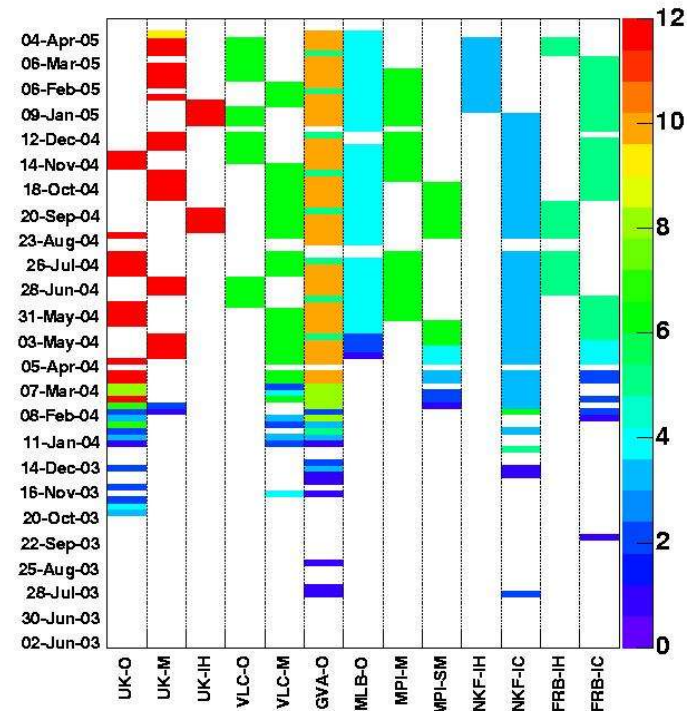

Wheels

- We assume a contingency of 15%, which is close to our actual yield
- 8C may have to wait for short middles
- 7A, 3C, 2C and 1C: all scheduled within one month

Endcap

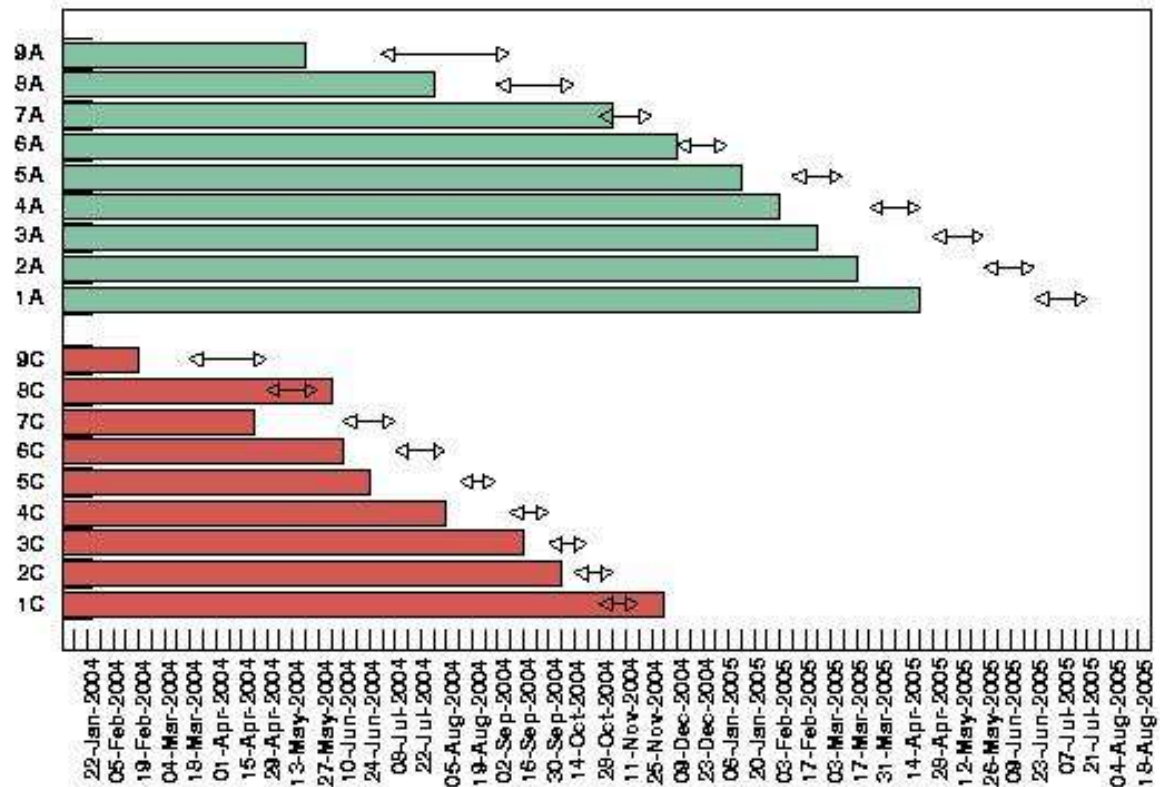

Components

- Components should be able to follow this assumption
 - ✓ Hybrids and Fan-ins have shown they can maintain the “expected” rate
 - ✓ Spines: **critical**
 - ✧ No extra delays allowed, otherwise: problems !!!

Stock of components

